
Activity ID	Activity Name	BL Project Duration	BL Project Start	BL Project Finish	Actual %	Planned %
Dammam 3rd Industrial City Gates and Fence - B1		75	06-May-26	05-Aug-26	88.7%	100%
Key Milestones		75	06-May-26	05-Aug-26	0%	0%
Mobilization		18	06-May-26	31-May-26	0%	0%
Preliminary Submittals		17	06-May-26	25-May-26	0%	0%
Engineering		49	18-May-26	18-Jul-26	100%	100%
Procurement		55	02-Jun-26	04-Aug-26	100%	100%
Construction		62	21-May-26	05-Aug-26	97.12%	100%
	SITE WORKS	61	21-May-26	05-Aug-26	94.49%	100%
	MASONRY UNIT	3	02-Jul-26	06-Jul-26	100%	100%
	THERMAL & MOISTURE PROTECTION	14	14-Jul-26	30-Jul-26	100%	100%
	ROOFING SYSTEM	11	18-Jul-26	30-Jul-26	100%	100%
	FINISHES	27	06-Jul-26	05-Aug-26	98.36%	100%
	SPECIAL CONSTRUCTION- STRUCTURAL STEEL (Fence Type 2)	30	02-Jul-26	05-Aug-26	98.33%	100%
	MECHANICAL WORKS	52	07-Jun-26	05-Aug-26	100%	100%
	ELECTRICAL WORKS	52	07-Jun-26	05-Aug-26	99.09%	100%
	METALS	2	04-Aug-26	05-Aug-26	100%	100%
	WOODS AND PLASTICS	3	03-Aug-26	05-Aug-26	100%	100%
	DOORS & WINDOWS	7	29-Jul-26	05-Aug-26	100%	100%
	SPECIALTIES	2	04-Aug-26	05-Aug-26	100%	100%
	FURNISHINGS	1	05-Aug-26	05-Aug-26	100%	100%
Testing & Commissioning		4	02-Aug-26	05-Aug-26	41.5%	100%
Handing Over		6	30-Jul-26	05-Aug-26	0%	100%

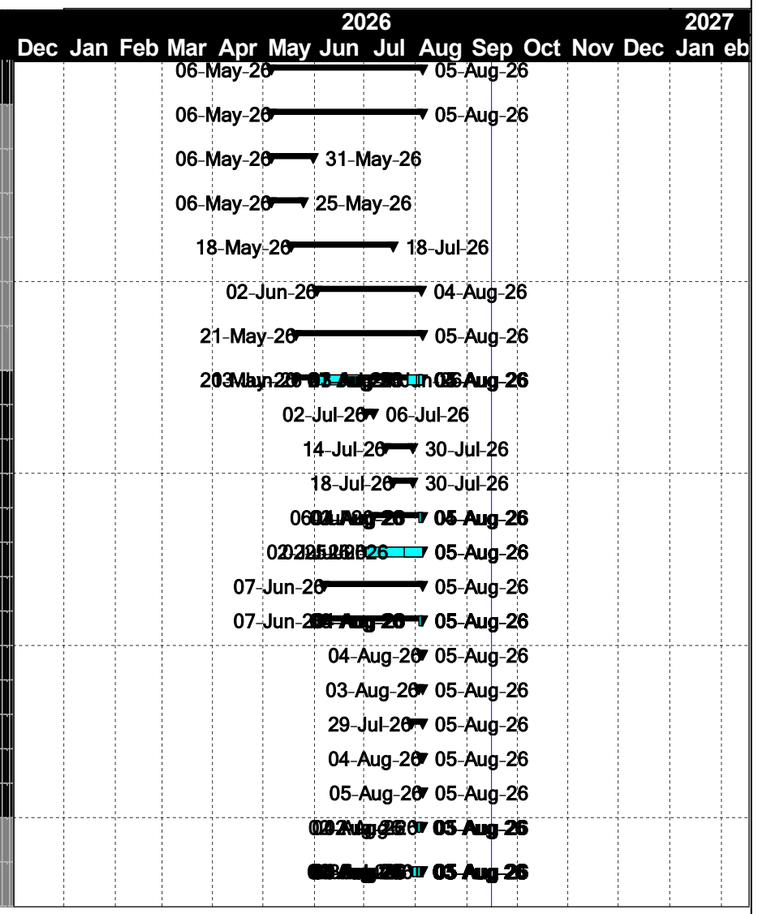

Actual Level of Effort
Actual Work
Remaining Work
Critical Remaining Work
Milestone
summary

TASK filter: All Activities

© Oracle Corporation
